

Team 4 & Sprint Project: Student Project Portfolio & Showcase App

NAME : KARANAM SREEHITHA SRN : PES1UG24AM129 SECTION : C

Lab 2 – Agile Backlog Creation & Sprint Simulation

Sprint: Sprint 2

1.Epic: Public Voting

Description:

This epic focuses on enabling public participants to view eligible projects, cast votes, validate votes, and receive confirmation after successful vote submission.

2.User Stories and Story Points

Issue	User Story	Story Points
SCRUM-22	View Projects for Voting	3
SCRUM-23	Cast a Public Vote	5
SCRUM-24	Validate Public Vote	5
SCRUM-25	Record and Confirm Vote	3
Total		16

Figure 1: Public Voting User Stories and Story Point Estimates

Atlassian uses cookies to improve your browsing experience, perform analytics and research, and conduct advertising. Accept all cookies to indicate that you agree to our use of cookies on your device. [Atlassian cookies and tracking notice](#)

Preferences Only necessary ☒ Accept all

Jira

Search

+ Create Premium trial

Spaces

Student Project Portfolio & Showcase App

Summary Backlog Board Docs Development Reports

Search backlog Filter

SCRUM-22 View Projects for Voting Public Voting To Do 3

SCRUM-23 Cast a Public Vote Public Voting To Do 5

SCRUM-24 Validate Public Vote Public Voting To Do 5

SCRUM-25 Record and Confirm Vote Public Voting To Do 3

+ Create

SCRUM Sprint 3 Add dates (0 work items) 0 0 0 Start sprint


Plan a sprint by dragging work items into it, or by dragging the sprint footer.

+ Create Quickstart

3. Sprint 2 Planning

The four Public Voting user stories were assigned to Sprint 2 along with the four Project Leaderboard stories created by the team. The Sprint 2 backlog therefore contained 8 work items.

Figure 2: Sprint 2 Backlog with Public Voting and Project Leaderboard Stories

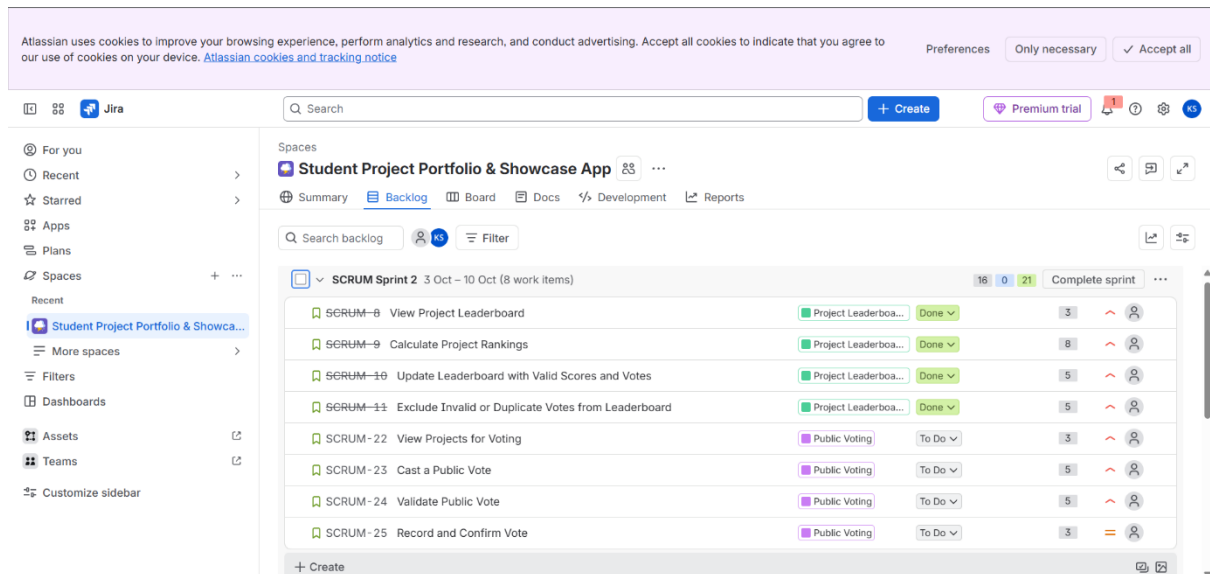

Project Leaderboard: $3 + 8 + 5 + 5 = 21$ points

Public Voting: $3 + 5 + 5 + 3 = 16$ points


Sprint 2 total: 37 story points

4. Sprint Simulation

The sprint was simulated by moving the work items through the Jira workflow from


To Do → In Progress → Done. All 8 work items were successfully completed.

Figure 3 — Final Sprint 2 Active Board

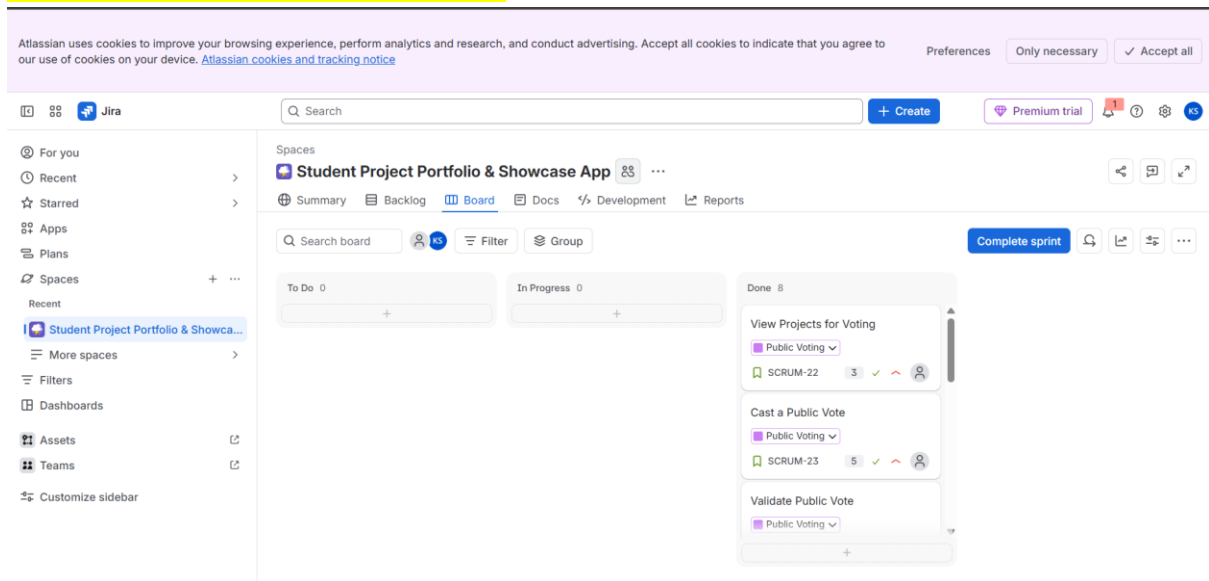

5. Burndown Chart

Sprint Burndown Chart

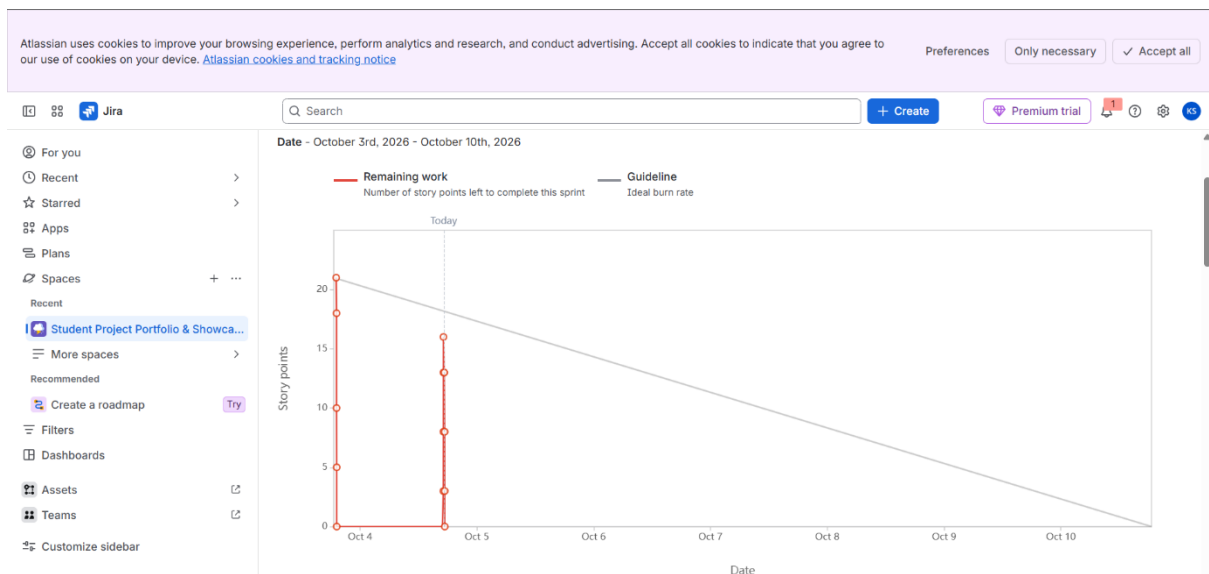

The Sprint Burndown Chart shows the remaining story points throughout Sprint 2. The red line represents the remaining work, while the grey line represents the ideal burn rate. The remaining work reached zero after all sprint items were completed. The chart also reflects the scope change caused by adding the Public Voting stories after the sprint had started.

6. Reflection

1. Did your estimations reflect the actual effort?

The Fibonacci story-point estimates provided a reasonable representation of the relative effort of the user stories. The simpler viewing and confirmation stories were assigned 3

points, while voting and validation activities were assigned 5 points because they involved more processing and validation.

2. Was your backlog well-prioritized?

Yes. The backlog was organized according to the functionality required for public voting. Viewing eligible projects was considered first, followed by casting, validating, and confirming the vote.

3. How did your simulated sprint align with your plan?

The simulated sprint followed the planned workflow of moving stories from To Do to In Progress and then Done. All 8 Sprint 2 work items were completed successfully.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart showed that the team completed the planned work and reached zero remaining story points. It also highlighted a scope increase of 16 story points when the Public Voting stories were added after the sprint started. This shows the importance of keeping sprint scope stable and planning work before the sprint begins.
